

AI-Assisted Reel Production Automation

A human-controlled workflow for faster, structured short-form video production

SUBMITTED FOR STAKEHOLDER REVIEW | JUNE 2026

PROPOSED INITIATIVE

Proposal at a glance

AgentR proposes a practical production workflow that turns a raw story into a reviewable reel package while the creator checks, corrects, and approves the important parts.

DECISION REQUEST Approve a small implementation test to set up the workflow, check quality, and measure time saved before any wider rollout.

BUSINESS NEED

Reduce repetitive preparation across scripting, scenes, prompts, timing, and assembly.

PROPOSED SOLUTION

AI prepares the production package; the creator reviews and approves it.

EXPECTED OUTCOME

Faster preparation, clearer structure, and traceable creator control.

01 / EXECUTIVE SUMMARY

A practical automation initiative with human editorial control

Short-form video production requires repeated effort across story restructuring, script drafting, scene planning, prompt preparation, visual review, dialogue timing, and assembly. These tasks slow output and make consistency difficult when handled independently.

PROPOSAL OBJECTIVE

Set up a repeatable AgentR workflow that turns a raw story into a reviewable draft while the creator keeps final editorial control.

In simple terms, AI prepares the production package, and the creator checks and approves the important parts.

What is being proposed

Structured production workflow A consistent sequence for story, script, scenes, prompts, visuals, dialogue, timing, and draft.	Human approval points Creator review at script, visual, timing, correction, and publish-readiness stages.
Reusable production assets Standard templates, scene formats, prompt rules, file conventions, and evidence records.	Measured test Track time, corrections, quality, consistency, and completion during the test.

Expected business value

Value area	Expected contribution
Efficiency	Reduce repeated preparation work and shorten the path to a first reviewable draft.
Consistency	Apply a common structure to scripts, scenes, prompts, captions, and timing plans.
Control	Keep creators responsible for factual accuracy, visual intent, corrections, and approval.
Scalability	Create a documented foundation that can be reused across more stories and teams.

What changes with AI-assisted reel production

How AI-Assisted Reel Production Will Help AgentR

1 Current Pain Points



3 Before vs After



KEY MESSAGE

3

02 / PROPOSED SOLUTION

One connected workflow from source material to reviewable draft

The proposed solution organizes production into eight clear stages. Each stage creates a useful output and includes a review point before the next stage is finalized.

STAGE 1 Story intake	STAGE 2 Script draft	STAGE 3 Script review	STAGE 4 Scene breakdown
STAGE 5 Prompts and visuals	STAGE 6 Dialogue and timing	STAGE 7 Draft assembly	STAGE 8 Correction and approval

How the workflow stays practical

Human review by design AI prepares structured options; the creator reviews, corrects, and approves.	Measure before scaling Any time or quality claim must be supported by the test records.
Plain-language control Creators request scene, visual, timing, and caption changes in normal language.	Improve one step at a time Each production stage can improve without redesigning the full workflow.


Who does what

Role	Responsibility
AgentR supports	Drafting, structuring, scene preparation, timing plans, and assembly support.
Creator controls	Source verification, editorial angle, visual judgment, corrections, and publication approval.

SIMPLE RULE	AI handles repeatable preparation. The creator makes the important accuracy, creative, and publishing decisions.
--------------------	--

VISUAL / TRANSFORMATION

From manual overload to scalable creative production

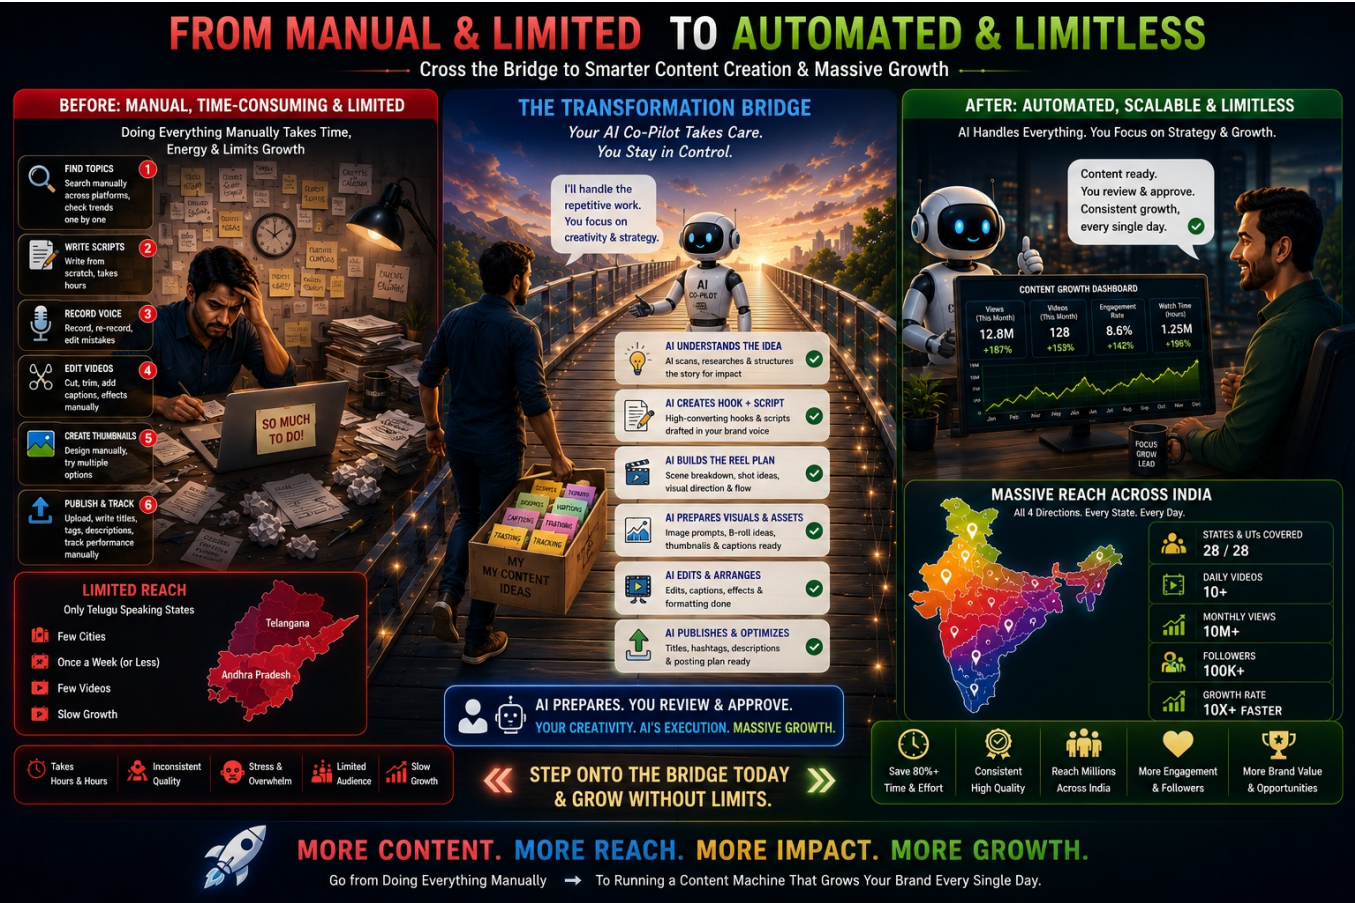

The left side shows the current manual burden, the center shows the human-guided automation bridge, and the right side shows the intended future state: more consistent output without removing creator control.

BUSINESS INTENT

Reduce repetitive work so more time can be invested in story quality, editing, audience growth, and brand partnerships.

03 / SCOPE AND DELIVERABLES

Clear outputs for the implementation phase

The first implementation phase will set up a working production system and confirm that it is useful before any decision to scale.

Workstream	Primary deliverables	Acceptance basis
Workflow design	Process map, stage owners, review points, and file conventions.	Approved process with clear handoffs.
Story and script	Intake template, script structure, fact checklist, and revision method.	Creator can approve a structured script.
Scene production	Scene format, prompt format, visual references, and regeneration rules.	Scenes trace to approved script content.
Dialogue and timing	Voiceover lines, duration plan, caption rules, and timing sheet.	Timing is understandable and editable.
Draft preparation	Reviewable draft, correction log, version history, and approval record.	Corrections can be requested and verified.
Measurement	Time log, correction categories, quality scorecard, and tracking sheet.	Results can be compared across productions.

What the client will receive

Client will receive	Meaning
Story intake format	A clear way to start each video
Script and scene template	Faster story-to-video planning
Image prompt format	Easier visual generation
Timing sheet	Clear dialogue and duration plan
Reviewable draft workflow	Faster first draft creation
Correction log	Clear record of changes
Measurement sheet	Time, quality, and correction tracking

VISUAL / OPERATING MODEL

How the human-guided automation workflow works



The workflow moves through idea intake, script and hook, scene structure, visual planning, edit-package creation, publish planning, and performance learning. Human review remains strongest where judgment and risk matter most.

CONTROL PRINCIPLE

AI prepares and learns from approved patterns. The creator retains critical decisions, corrections, and final publishing authority.

04 / TEST PLAN AND EVIDENCE

A controlled 10-15 reel test before scaling

The proposal begins with a small test rather than full automation. The purpose is to confirm that the workflow saves time, preserves quality, and keeps the creator in control.

This size is small enough to control risk but large enough to confirm whether the workflow works across different story types.

Test size 10-15 representative reels across a defined content mix.	Duration Approximately 2-3 weeks, subject to reviewer availability.	Decision rule Scale only if time improves and quality is maintained.
--	---	--

How evidence will be used

Evidence layer	Purpose
Baseline	Capture current time per reel, script time, corrections, editing preparation, and quality score.
Test records	Retain scripts, scene plans, prompts, timing sheets, drafts, corrections, and approvals.
Evaluation	Compare production effort, correction load, quality, and human approval checks.
Decision support	Use measured results to recommend revise, extend, scale, or stop.

What counts as success

Measure	Success target
Time reduction	40% or more
Reviewable drafts	At least 80% of tested reels
Quality score	4/5 or better
Human approval	100% before publishing
Critical factual errors	Zero
Visual consistency	No major recurring issue

05 / CLIENT INPUTS NEEDED

What we need from the client before the test begins

A few clear inputs will help the team start quickly, protect the brand, and compare the new workflow fairly against the current process.

Client input needed	Why it is needed
Story/topic list	To choose reels for the test
Brand/content style preference	To keep output consistent
Reviewer availability	To approve scripts, visuals, and drafts
Existing manual time estimate	To compare before vs after
Publishing rules or restrictions	To avoid sensitive or unsuitable output

Start readiness checklist

Content set confirmed
The 10-15 test stories represent the content types the client actually wants to produce.

Reviewer confirmed
One named person can review scripts, visuals, corrections, and final drafts.

Rules documented
Brand preferences, sensitive-content rules, and publishing restrictions are available.

Baseline available
Current time estimates or recent production records can be used for comparison.

SIMPLE ASK
Confirm these inputs before the start date so the controlled test can begin without avoidable delays.

06 / IMPLEMENTATION AND REVIEW

A simple four-step rollout with review points

The project moves through four clear steps. Each next step begins only after the agreed output is reviewed and accepted.

1 / Define
Confirm goals, roles, content rules, workflow stages, quality criteria, and the representative content set.

2 / Configure
Build templates, prompts, file structure, timing rules, review points, and measurement records.

3 / Test
Run the test reels, capture timings, document corrections, and conduct creator reviews.

4 / Evaluate
Assess quality, consistency, effort, safety, and repeatability; recommend revise, extend, or stop.

Who is responsible

Role	Primary responsibility
Project sponsor	Approves scope, resources, success criteria, and any later rollout.
Creator / editor	Approves scripts, visuals, timing, corrections, and publish readiness.
Workflow owner	Maintains templates, coordinates stages, records decisions, and resolves issues.
Quality reviewer	Checks accuracy, consistency, sensitive content, and scoring quality.

Non-negotiable safeguards

No automatic publishing
Every reel requires named human approval before release.

Clear revision history
Material changes and correction decisions are recorded by version.

Sensitive-content review
True-crime and other sensitive subjects receive editorial and safety review.

Measured results
Future performance claims are based on captured production records.

07 / SUCCESS MEASURES AND APPROVAL

Approve the small test against clear targets

What will be measured

Measure	How it will be assessed
Production effort	Actual time from approved story intake to first reviewable draft, recorded by stage.
Quality	Creator score covering accuracy, coherence, visual consistency, pacing, and readiness.
Correction load	Number and severity of factual, structural, visual, caption, and timing corrections.
Human approval	Completion of required creator reviews before publishing.
Repeatability	Ability to apply the workflow across different stories without a major process failure.

Main risks and responses

Risk	Proposed response
Factual or contextual error	Require source checks and script approval before visual production.
Visual inconsistency	Use reusable character, style, and location references.
Unmeasured time-saving claims	Capture timestamps and correction effort from the start.
Different reviewer standards	Use one scoring guide and shared examples.
Sensitive-content concerns	Maintain mandatory editorial review and explicit publish approval.

RECOMMENDED DECISION Approve the controlled 10-15 reel test. Next step: Confirm test content set, reviewer, timeline, and start date for the controlled 10-15 reel implementation test.

COMMERCIAL TERMS This approval is for controlled implementation planning and validation only. Final commercial terms, timelines, and scale-up scope will be confirmed separately.
